

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Cost	2012												2013											
									Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
1			Contract Design Firms	450 days	Tue 11/1/11	Mon 7/22/13		\$0.00																								
2			Finalize Project Scope	550 days	Tue 7/23/13	Mon 8/31/15	1	\$0.00																								
3			Preliminary Alignment	300 days	Tue 9/1/15	Mon 10/24/16	2	\$1,158,772.00																								
4			Access Justification Report	100 days	Tue 1/3/17	Mon 5/22/17	3	\$0.00																								
5			NEPA	450 days	Tue 9/1/15	Mon 5/22/17	2	\$223,000.00																								
6			Execute Agreements with Midwest City, Oklahoma City and Tinker Air Force Base	200 days	Tue 10/25/16	Mon 7/31/17	3	\$0.00																								
7			Finalize Functional Plans	100 days	Tue 10/25/16	Mon 3/13/17	3	\$1,200,000.00																								
8			Right Of Way Acquisition	0 days	Mon 5/22/17	Mon 5/22/17	7,5	\$0.00																								
9			Relocate Utilities	100 days	Tue 5/23/17	Mon 10/9/17	7,5	\$100,000.00																								
10			STIP/TIP Approval	90 days	Thu 9/1/16	Wed 1/4/17		\$0.00																								
11			Finalize Design Plans	150 days	Tue 3/14/17	Mon 10/9/17	7	\$900,000.00																								
12			Submit PS&E	50 days	Tue 10/10/17	Mon 12/18/17	11	\$0.00																								
13			Contracting for Construction	120 days	Tue 12/19/17	Mon 6/4/18	12,9	\$0.00																								
14			Reconstruct Douglas Interchange	600 days	Tue 6/5/18	Mon 9/21/20	13	\$35,000,000.00																								
15			Raise Post Road	30 days	Tue 6/5/18	Mon 7/16/18	13	\$1,000,000.00																								
16			Raise Westminster Road	30 days	Tue 7/17/18	Mon 8/27/18	15	\$1,000,000.00																								
17			Widen I-40 over I-240 Bridges	120 days	Tue 6/5/18	Mon 11/19/18	13	\$2,500,000.00																								
18			Redeck remaining I-40 over I-240 bridge	90 days	Tue 11/20/18	Mon 3/25/19	17	\$2,000,000.00																								
19			Counstruct Outside Eastbound Anderson Road Bridges	80 days	Tue 6/5/18	Mon 9/24/18	13	\$3,000,000.00																								
20			Build Inside Shoulder Eastbound	200 days	Tue 8/28/18	Mon 6/3/19	16	\$12,000,000.00																								
21			Rebuild outside lane and shoulder Eastbound	200 days	Tue 6/4/19	Mon 3/9/20	20	\$14,000,000.00																								
22			Reconstruct Westbound I-40	300 days	Tue 3/10/20	Mon 5/3/21	21,17,19	\$28,000,000.00																								

Project: CPM.mpp
Date: Thu 4/7/16

Task

Split

Milestone

Summary









Project Summary

External Tasks

External Milestone

Inactive Task









Inactive Milestone

Inactive Summary

Manual Task

Duration-only









Manual Summary Rollup

Manual Summary

Start-only

Finish-only









Deadline

Critical

Critical Split

Progress



ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Cost													2012												2013											
									Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov											
23			Construct Westbound I-40 Bridge over Anderson Road	120 days	Tue 3/10/20	Mon 8/24/20	21	\$6,000,000.00																																				
24			Construct Inside on Eastbound Anderson Road bridges	120 days	Tue 5/4/21	Mon 10/18/21	22,23	\$3,500,000.00																																				
25			Reconstruct Inside Eastbound Lanes	150 days	Tue 5/4/21	Mon 11/29/21	22	\$7,000,000.00																																				



Project: CPM.mpp
Date: Thu 4/7/16

Task



Project Summary



Inactive Milestone



Manual Summary Rollup



Deadline



Split



External Tasks



Inactive Summary



Manual Summary



Critical



Milestone



External Milestone



Manual Task



Start-only



Critical Split



Summary



Inactive Task



Duration-only




Finish-only




Progress




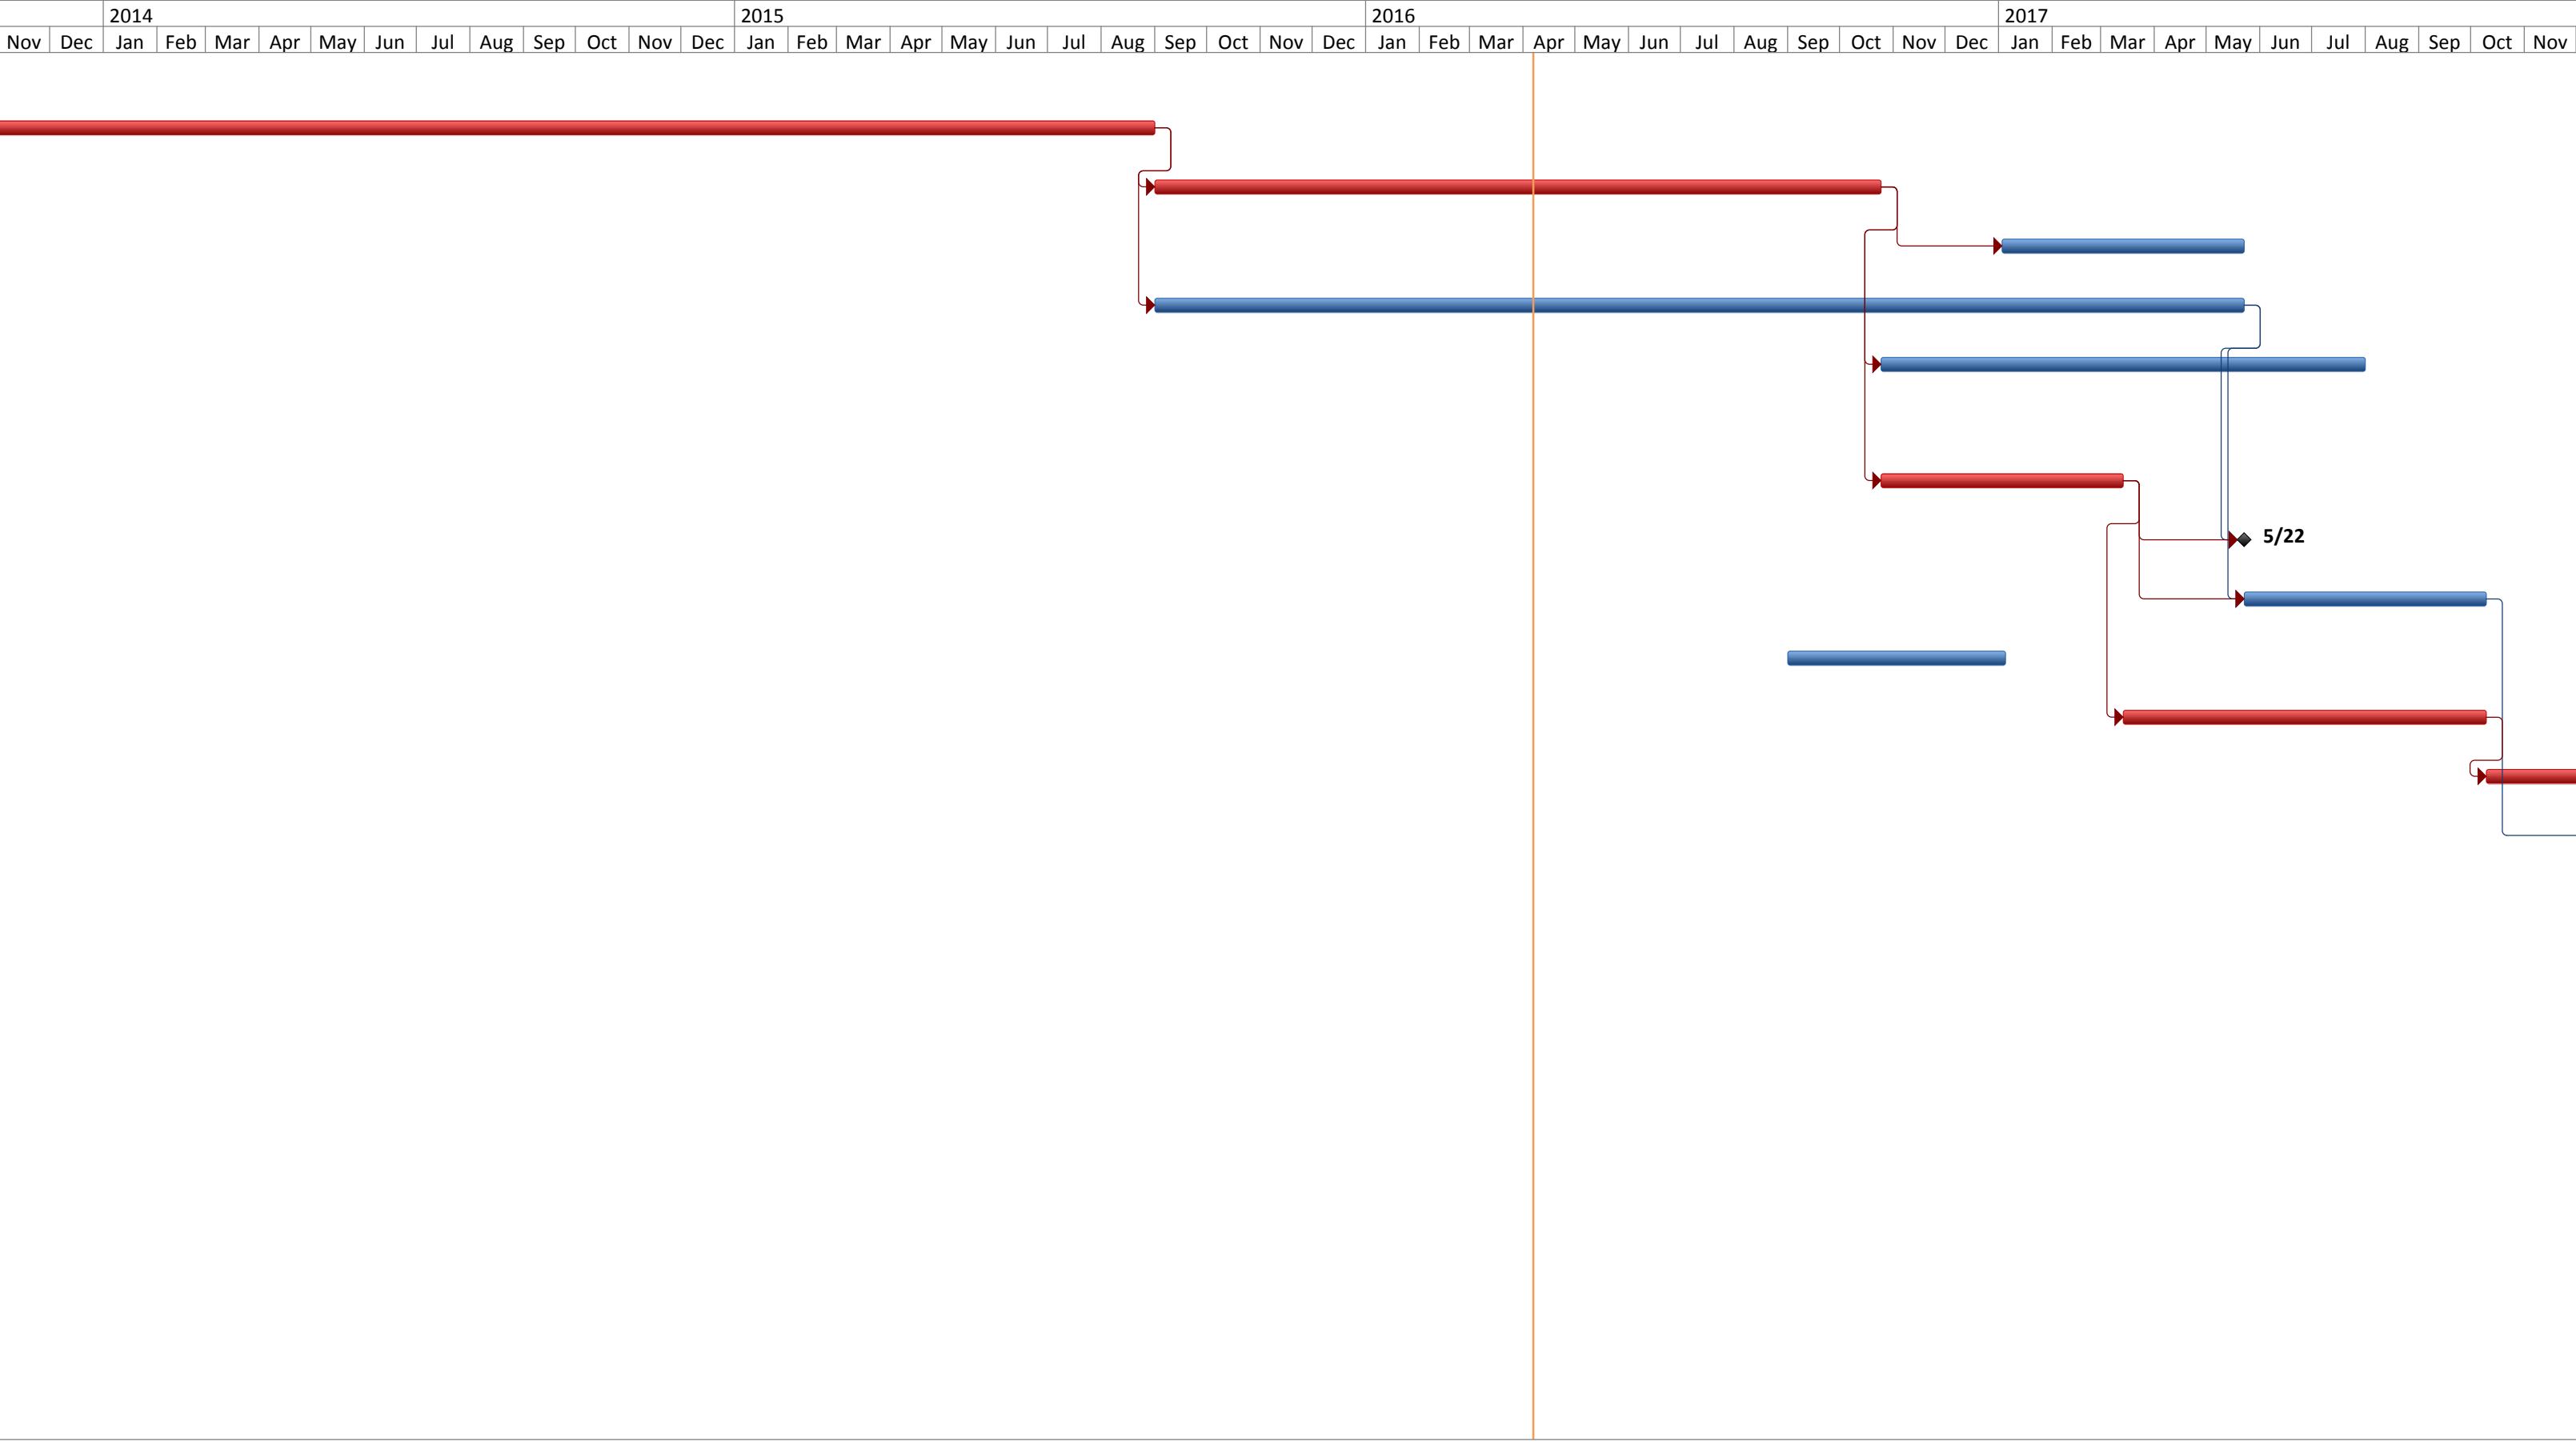

Project: CPM.mpp Date: Thu 4/7/16	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Critical	
	Milestone		External Milestone		Manual Task		Start-only		Critical Split	
	Summary		Inactive Task		Duration-only		Finish-only		Progress	



Project: CPM.mpp Date: Thu 4/7/16	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Critical	
	Milestone		External Milestone		Manual Task		Start-only		Critical Split	
	Summary		Inactive Task		Duration-only		Finish-only		Progress	

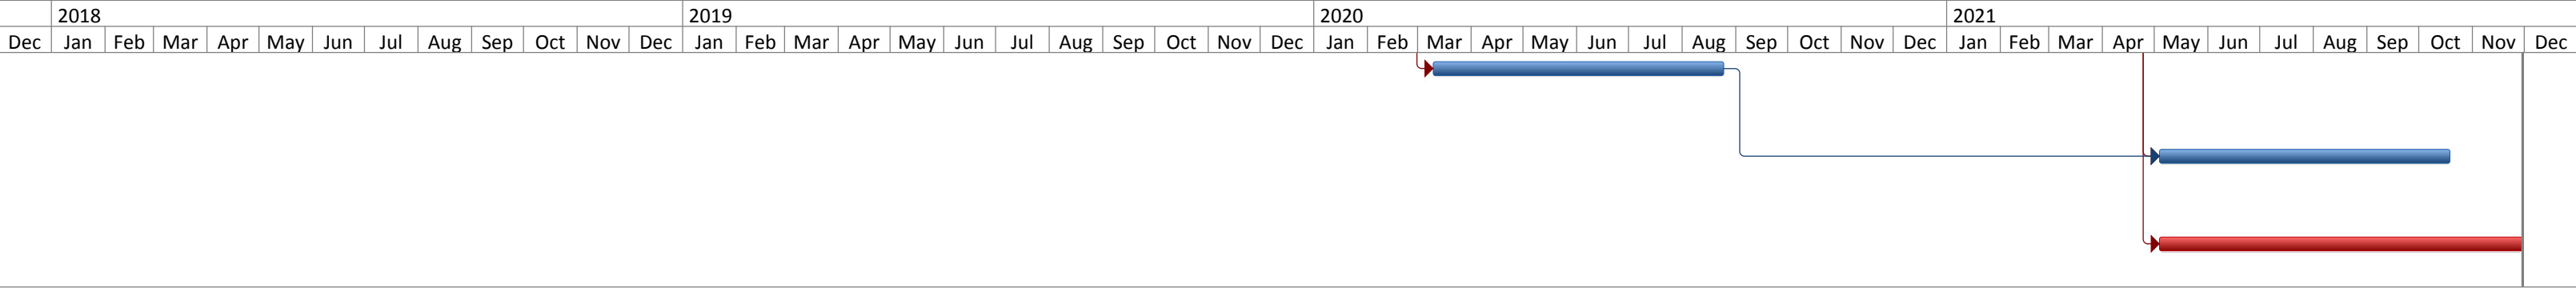

Project: CPM.mpp Date: Thu 4/7/16	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Critical	
	Milestone		External Milestone		Manual Task		Start-only		Critical Split	
	Summary		Inactive Task		Duration-only		Finish-only		Progress	
